


## EXHIBIT 10

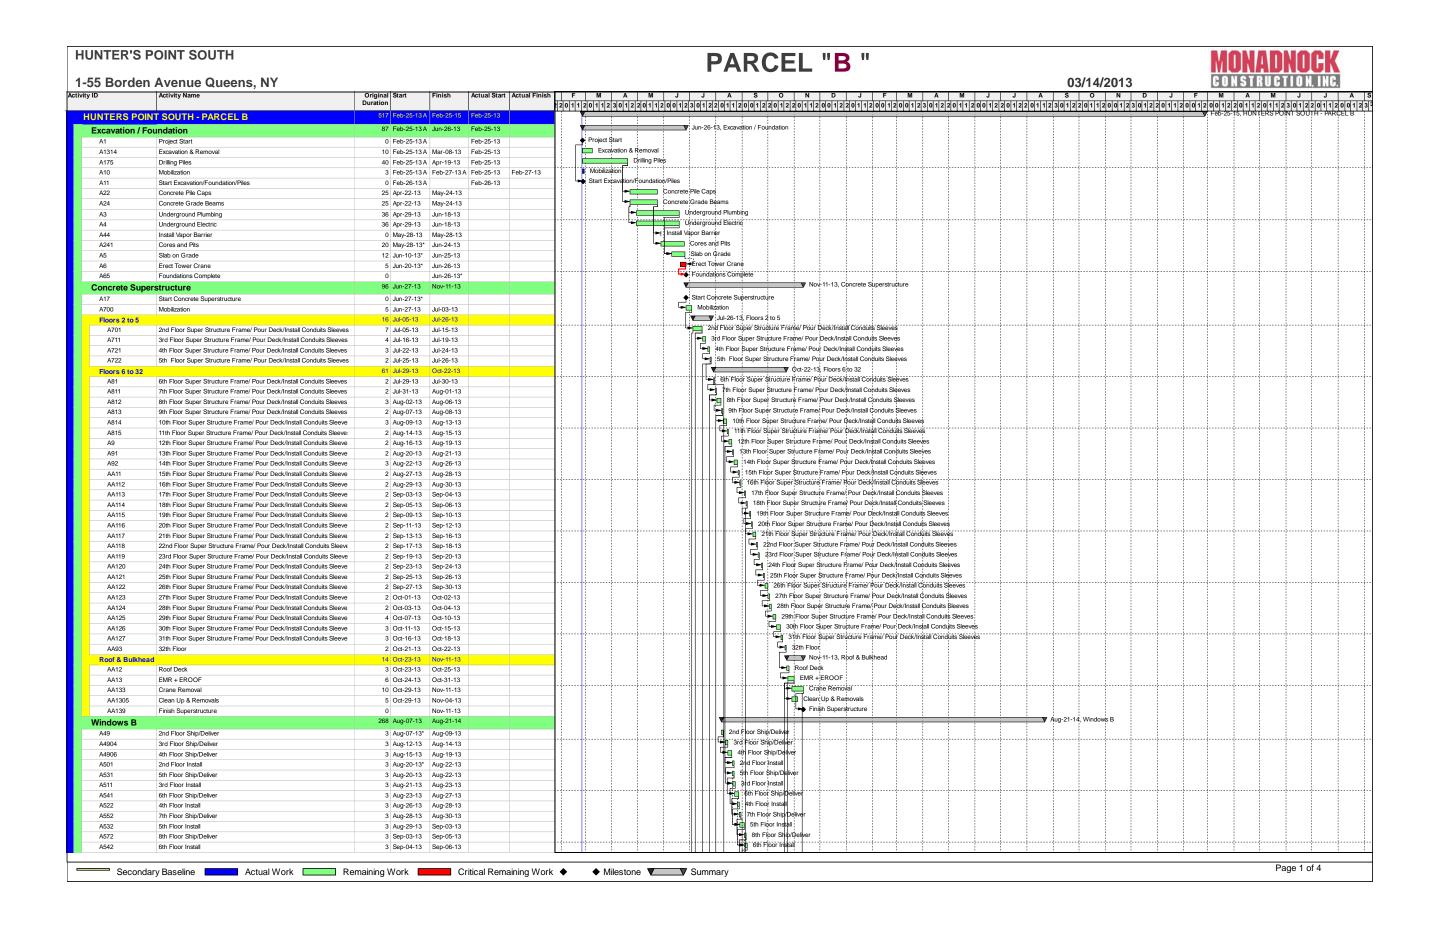

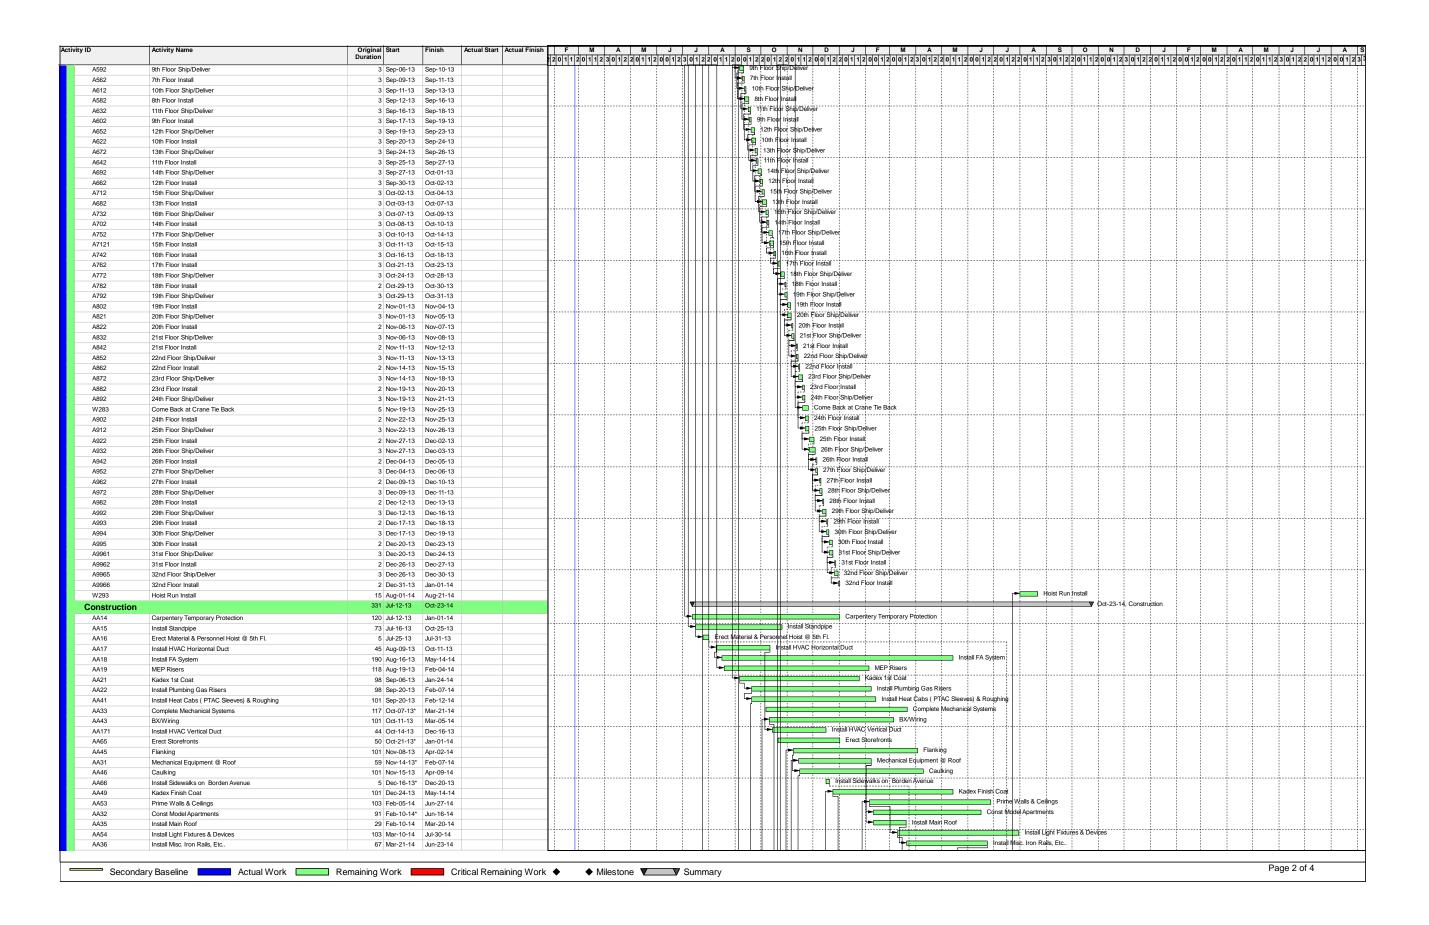

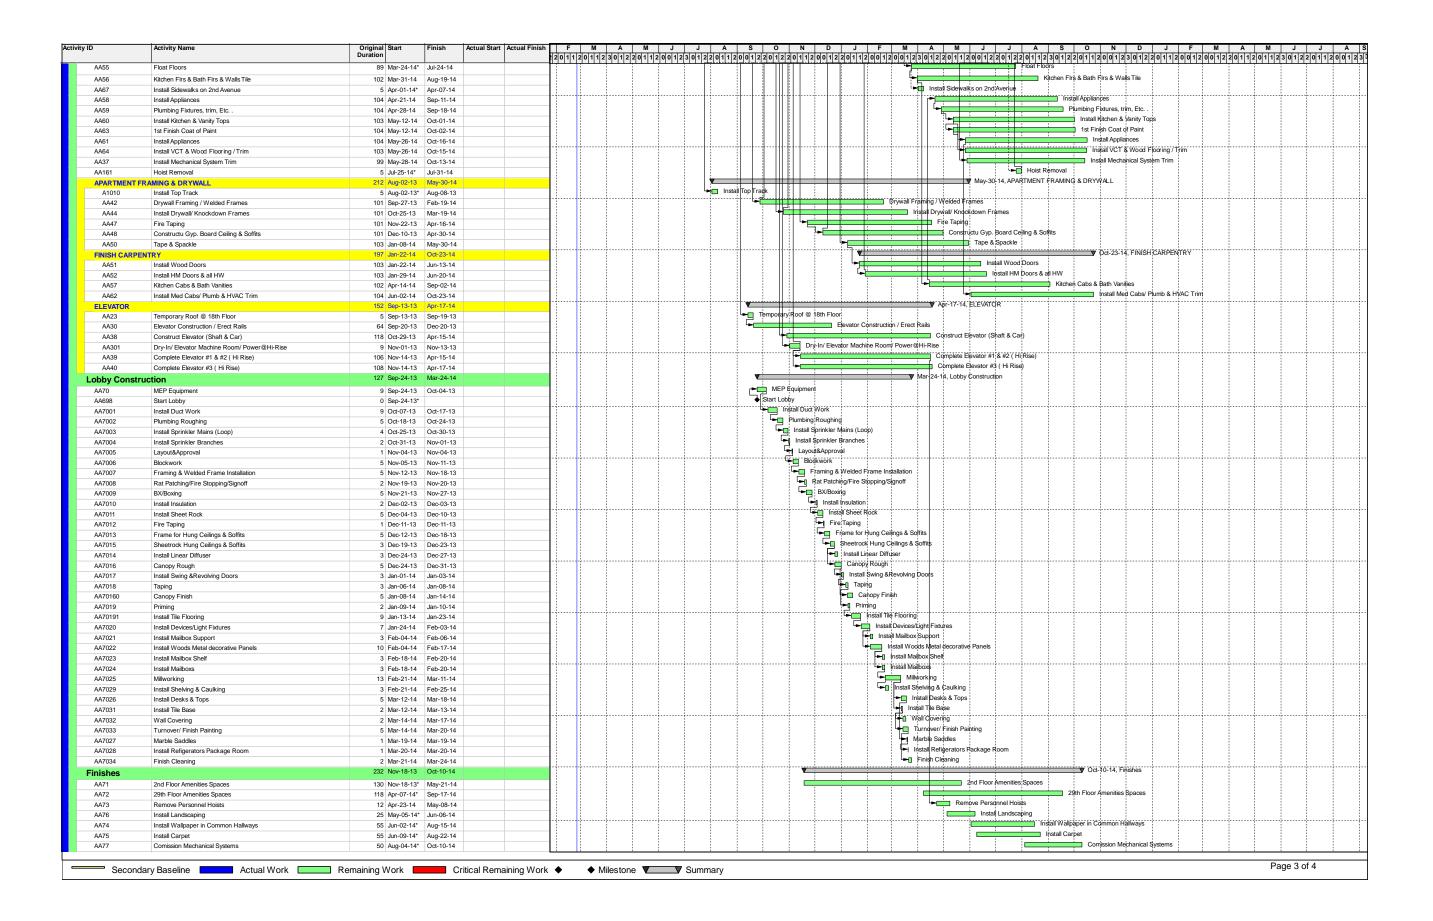

Confidential MC\_00000142

Activity ID	Activity Name	Duration	al Finish   F   M   A   M   J   J   A   S   O   N   D   J   F   M   A   M   J   J   A   S   O   N   D   J   F   M   A   M   J   J   A   S   O   N   D   J   F   M   A   M   J   J   J   A   S   O   N   D   J   F   M   A   M   J   J   J   A   S   O   N   D   J   F   M   A   M   J   J   J   A   S   O   N   D   J   F   M   A   M   J   J   J   A   S   O   N   D   J   F   M   A   M   J   J   J   A   S   O   N   D   J   F   M   A   M   J   J   J   A   S   O   N   D   J   F   M   A   M   J   J   J   A   S   O   N   D   J   F   M   A   M   J   J   J   A   S   O   N   D   J   F   M   A   M   J   J   J   A   S   O   N   D   J   F   M   A   M   J   J   J   A   S   O   N   D   J   F   M   A   M   J   J   J   A   S   O   N   D   J   F   M   A   M   J   J   J   A   S   O   N   D   J   F   M   A   M   J   J   J   A   S   D   N   D   J   J   A   S   D   N   D   J   J   A   S   D   N   D   J   J   A   S   D   N   D   J   A   S   D   A   S   D   N   D   J   A   S   D   A   S   D   A   A   S   D   A   A   A   A   A   A   A   A   A	2 0 1 1 2 3 0 1 2 2 0 1 1 2 0 0 1 2 3
Project Comple	ete	268 Feb-17-14 Feb-25-15	✓ Feb-25-15, Proj	edt Complete
AA79	Punchlist/ Finish Coat of Painting	180 Feb-17-14* Oct-24-14	Punchlist/Finish Cqut of Painting	
AA80	1st TCO Inspection - Firs 1-8	1 Jun-18-14 Jun-18-14	→ 1st TCO Inspection - Firs 1-8	· † · · · · · · † · · · · · · † · · · ·
AA81	Turnover Floors 1-4 Floors	19 Jun-25-14 Jul-21-14	turnover ‡loors 1-4 Floors	
AA82	Turnover Floors 5-8	20 Jul-22-14 Aug-18-14	- Tψrnover Floors 5-8	
AA83	2nd TCO-Firs 9-15	1 Aug-19-14* Aug-19-14	2nd TCO-Fits 9-15	
AA84	Turnover Floors 9-15	29 Aug-20-14 Sep-29-14	Turnover Floors 9-15	
AA86	3rd TCO Firs 16-32	1 Sep-30-14* Sep-30-14	1 3rd TCO Firs 16-32	
AA88	Turnover Floors 16-32	35 Oct-01-14* Nov-18-14	Turnover Floors 16-32	
AA89	Project Closeout	40 Nov-19-14 Jan-13-15	Project Closeout	
AA90	Project Completition	0 Feb-25-15*	→ Project Completi	tion
Seconda	ry Baseline Actual Work	Remaining Work Critical Remaining	g Work ♦ Milestone ✓ Summary	Page 4 of 4

Confidential MC\_00000143
